


# City of New Albany 2024 Street Maintenance F-0946-024

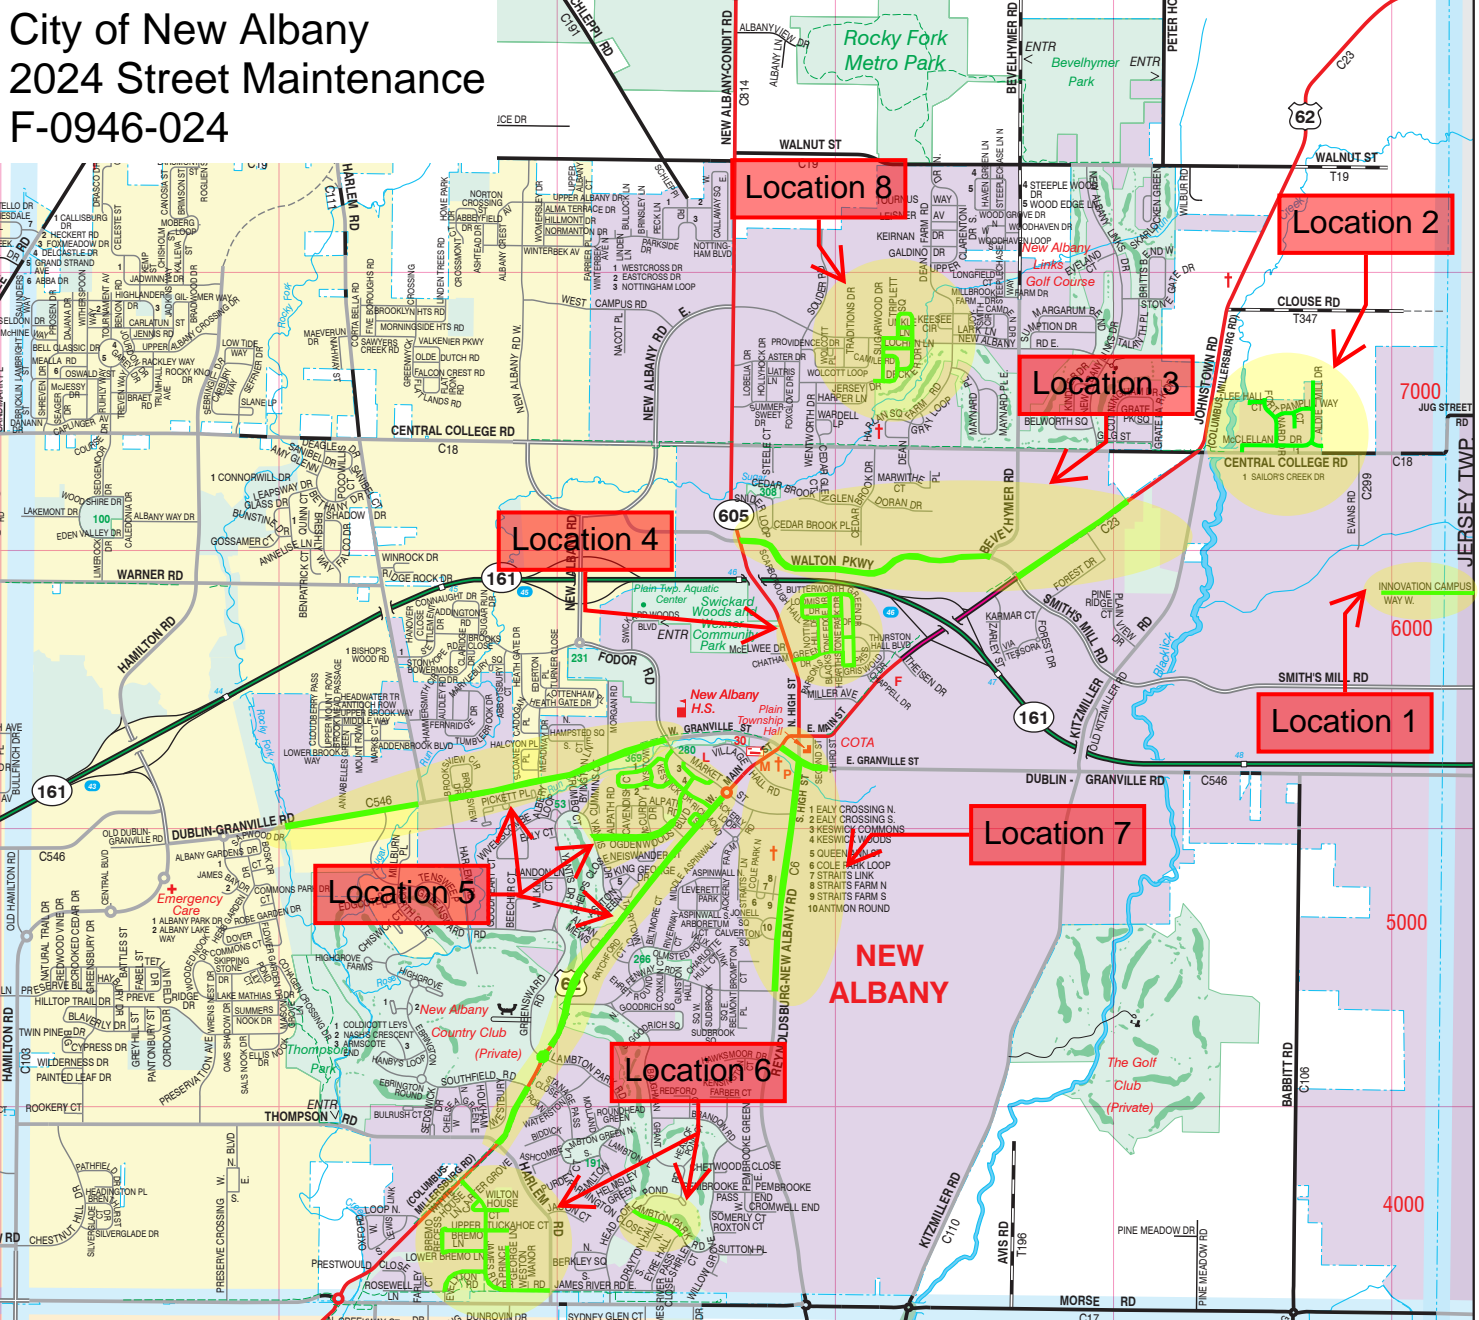

Location 8

Location 2

Location 3

Location 4

Location 1


Location 5

Location 7

Location 6


# Location 1 MOT Plan

Location 1						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
22	Innovation Campus Way	9/16-9/20	9/23-9/24	9/25-9/26	12,019	1,002
23	Innovation Campus Way	9/16-9/20	9/24	9/26	2,561	213

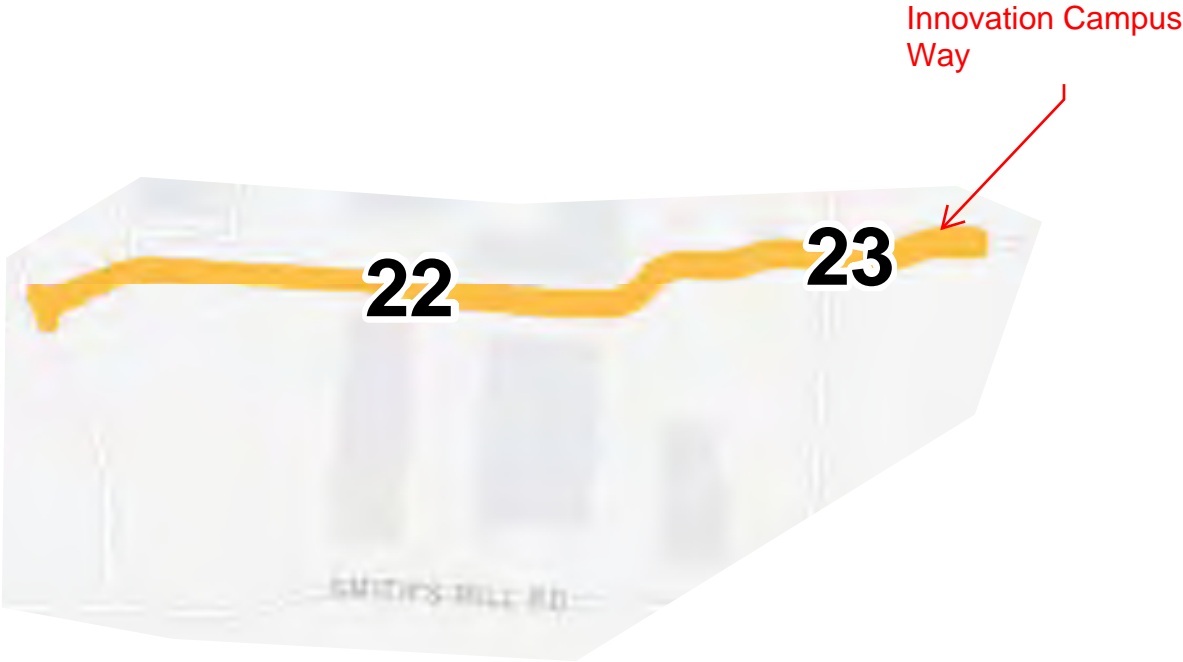


# Location 2 MOT Plan

Location 2						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
1	Aldie Mill Dr	Complete	8/27	9/3	3,051	254
19	Fort Ward Dr.	Complete	8/27	9/3	2,659	222
36	Lee Hall Ct	Complete	8/28	9/4	1,555	130
39	McClellan Dr.	Complete	8/28	9/4	5,456	455
45	Pamplin Ct.	Complete	8/29	9/5	1,459	122
46	Pamplin Way	Complete	8/29	9/5	2,001	167
50	Sailors Creek Dr.	Complete	8/29	9/5	862	72

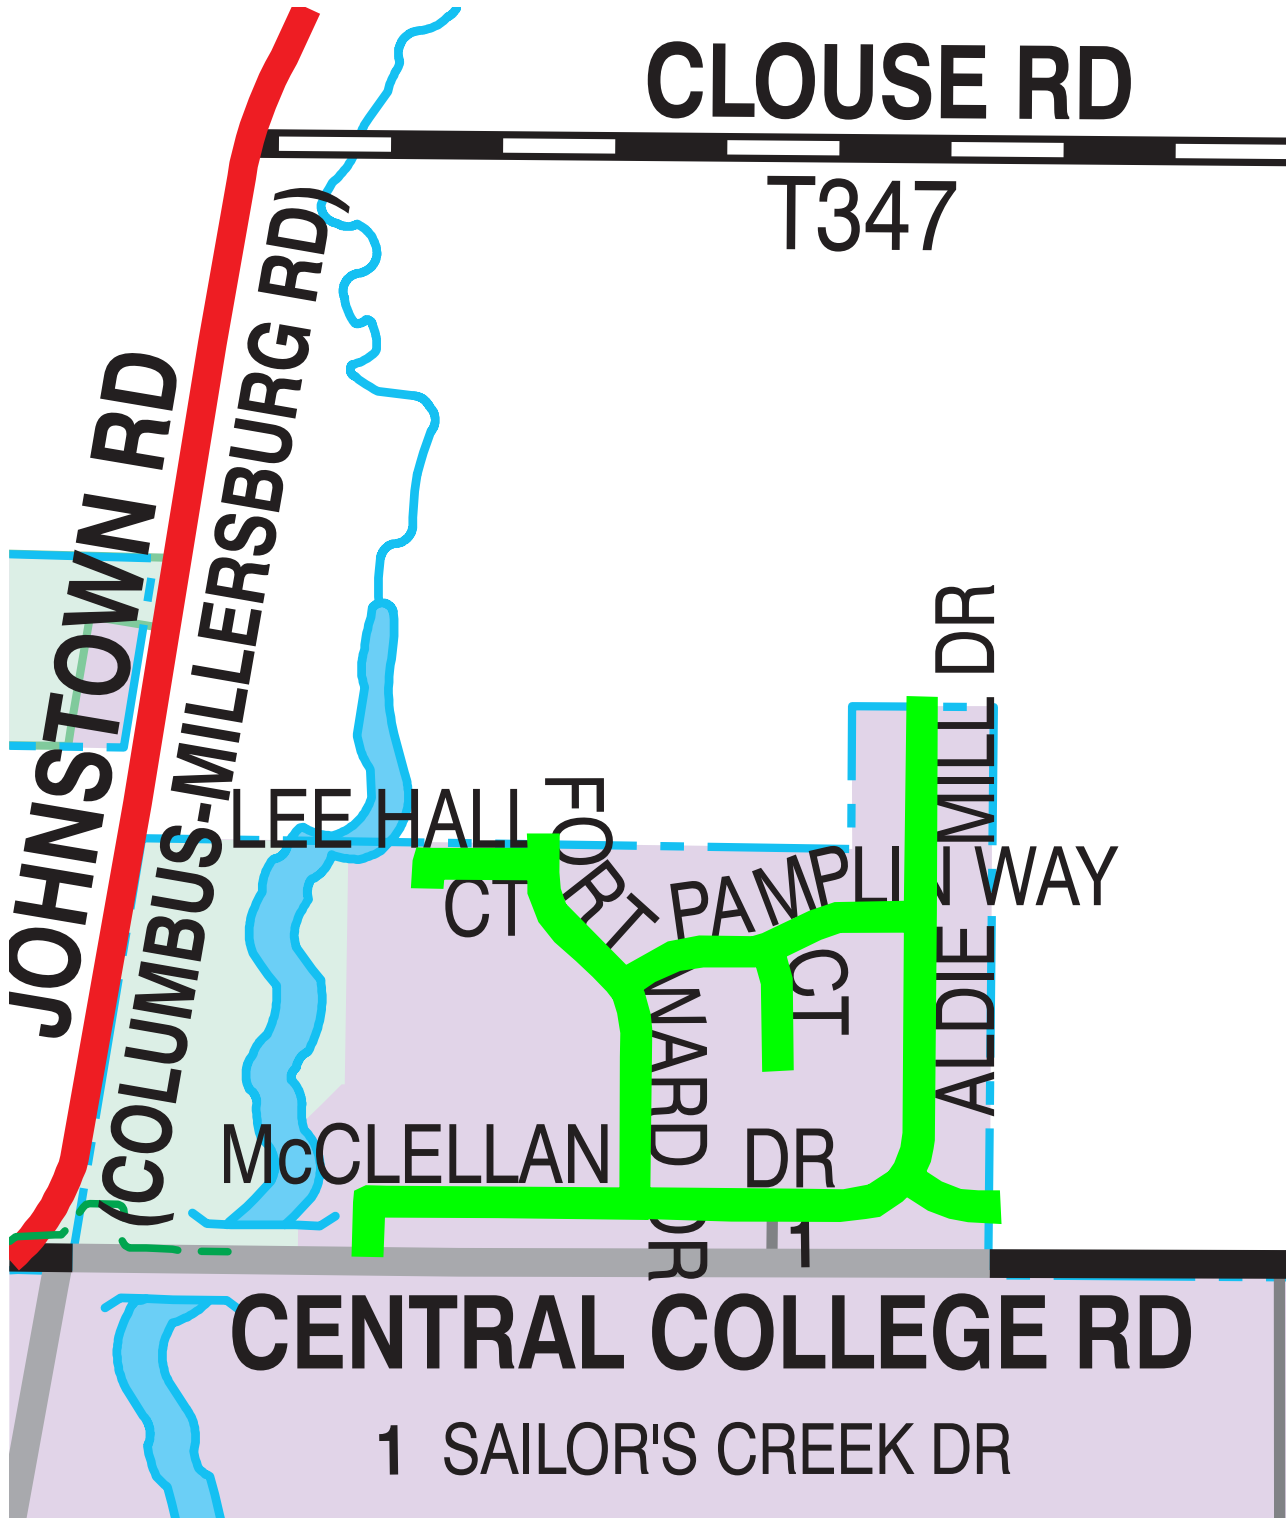

# Location 3 MOT Plan


Location 3						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
28	Johnstown Rd.	9/23-9/27	9/25-9/26	9/27-9/30	14,672	1,223
57	Walton Pkwy	9/23-9/27	9/27-9/30	10/1	20,177	1,681

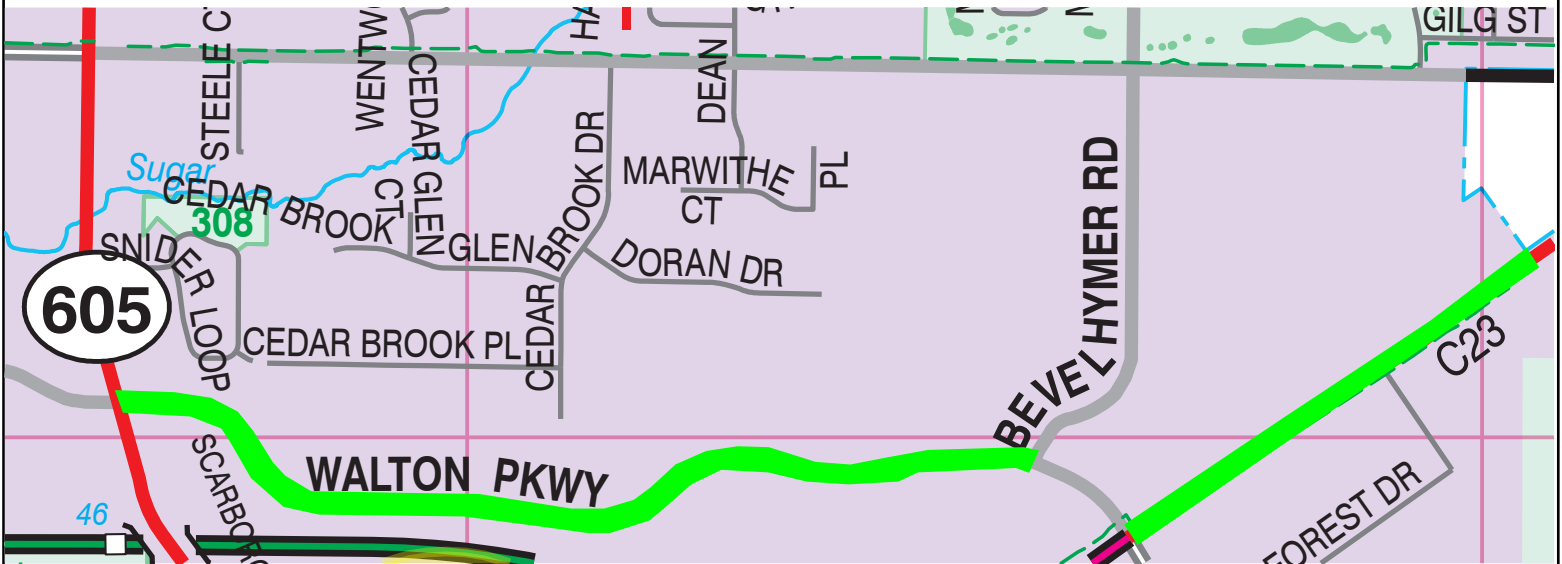




# Location 4 MOT Plan

Location 4						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
2	Blackstone Edge Dr.	9/3-9/6	9/12	9/14	1,909	159
3	Blackstone Edge Dr.	9/3-9/6	9/12	9/14	1,221	102
4	Bremo Recess	9/3-9/6	9/12	9/14	2,167	181
5	Butterworth Green Dr.	9/3-9/6	9/13	9/15	1,426	119
6	Butterworth Green Dr.	9/3-9/6	9/13	9/15	2,110	176
7	Butterworth Green Dr.	9/3-9/6	9/13	9/15	1,760	147
8	Butterworth Green Dr.	9/3-9/6	9/16	9/19	791	66
11	Chatham Green Dr.	9/3-9/6	9/16	9/19	3,180	265
21	Hearthstone Park Dr.	9/3-9/6	9/16	9/19	3,780	315
37	Loomis Dr.	9/3-9/6	9/17	9/20	1,541	128
42	Nottingham Dr.	9/3-9/6	9/17	9/20	1,984	165
51	Scarborough Hall Dr.	9/3-9/6	9/17	9/20	3,758	313

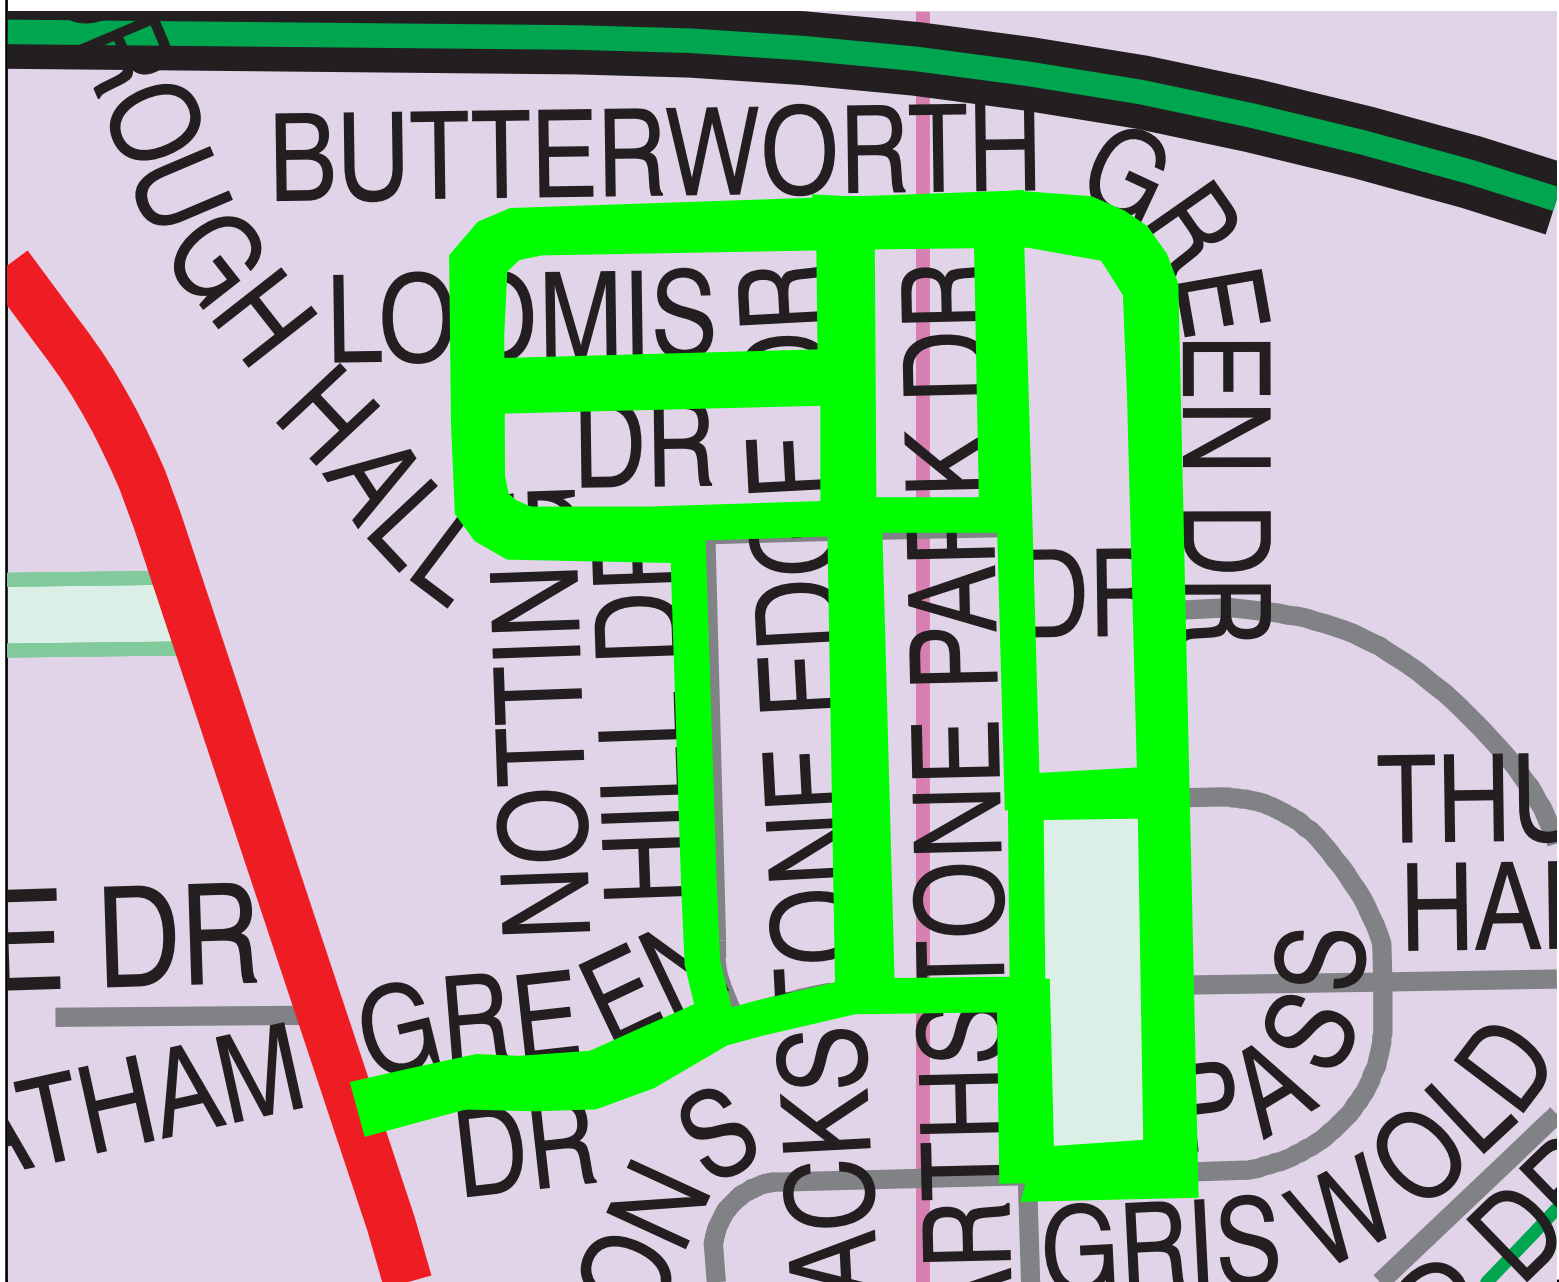


# Location 5 MOT Plan

Location 5						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
13	E. Dublin- Granville Rd	Complete	Complete	Complete	6,941	578
14	E. Dublin- Granville Rd	Complete	8/26	8/27-8/28	14,185	1,182
16	Ealy Crossing Dr N	Complete	Complete	Complete	2,891	241
17	Ealy Crossing Dr S	Complete	Complete	Complete	3,152	263
20	Hays Town	Complete	Complete	Complete	813	68
26	Johnstown Rd.	Complete	Complete	Complete	5,355	446
27	Johnstown Rd.	Complete	9/3	9/6-9/9	17,933	1,494
29	Johnstown Rd.	Complete	9/21	9/22	234	20
30	Keswick Commons	Complete	Complete	Complete	1,822	152
31	Keswick Dr.	Complete	Complete	Complete	1,928	161
32	Keswick Woods	Complete	Complete	Complete	1,117	93
33	Kieswick Dr.	Complete	Complete	Complete	2,643	220
40	McDonald Ln.	Complete	Complete	Complete	2,003	167
41	McDonald Ln.	Complete	Complete	Complete	673	56
49	Richmond Sq.	Complete	Complete	Complete	1,305	109
43	Ogden Woods Blvd.	Complete	Complete	Complete	8,585	715
44	Ogden Woods Blvd.	Complete	Complete	Complete	2,742	228

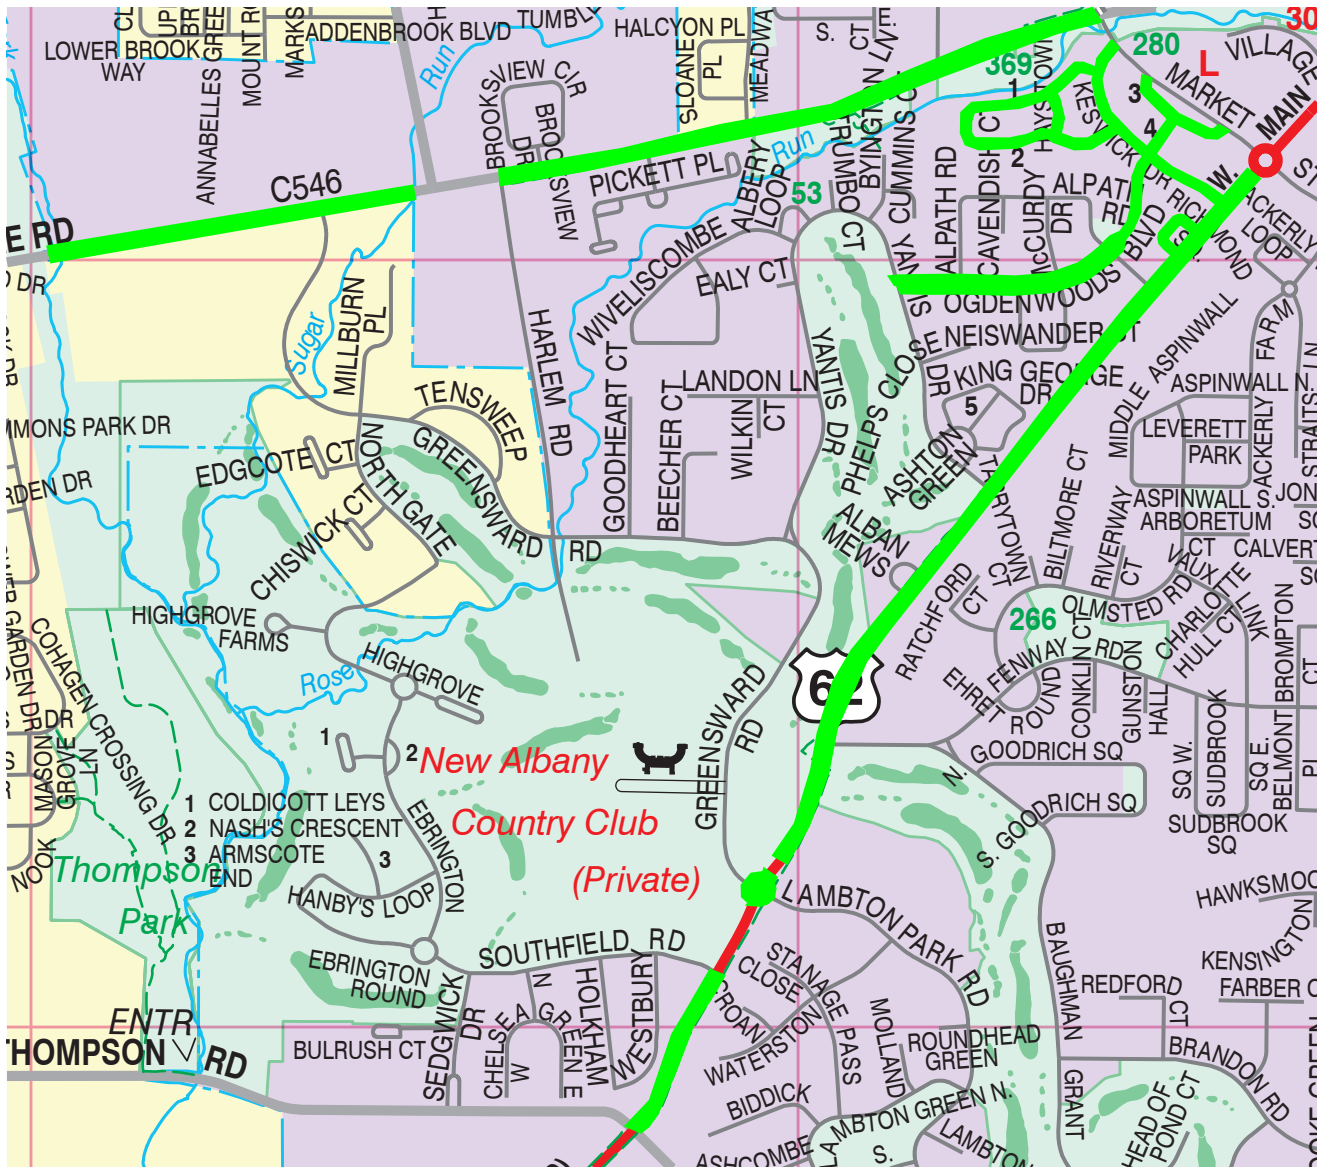


# Location 6 MOT Plan

Location 6						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
10	Carters Grv	Complete	Complete	Complete	1,417	118
18	Evelyton Rd.	Complete	Complete	Complete	3,988	332
24	James River East	Complete	Complete	Complete	10,532	878
34	Lambton Park Rd.	Complete	Complete	Complete	2,803	234
35	Lambton Park Rd.	Complete	Complete	Complete	156	13
38	Lower BreMO Ln.	Complete	Complete	Complete	2,207	184
47	Prince George Ln.	Complete	Complete	Complete	3,208	267
54	Tuckahoe Ct.	Complete	Complete	Complete	1,680	140
55	Upper BreMO Ln.	Complete	Complete	Complete	2,201	183
58	Weston Mnr.	Complete	Complete	Complete	741	62
59	Wilton House Ct.	Complete	Complete	Complete	1,664	139

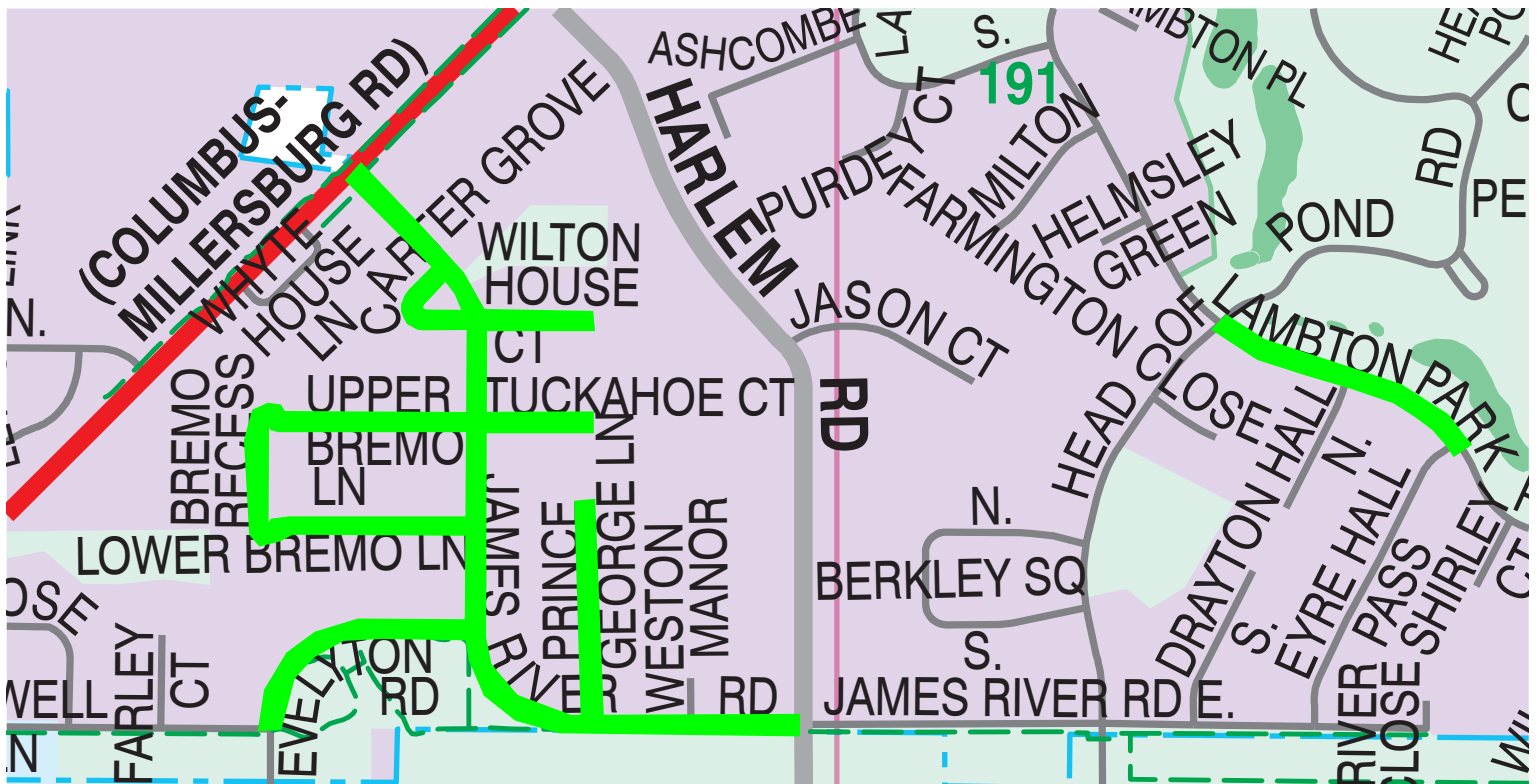


# Location 7 MOT Plan

Location 7						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
15	E. Dublin- Granville Rd	8/26-9/6	9/10	9/12	1,353	113
48	Reynolds-NA RD	Complete	Complete	8/27	14,737	1,228
56	W Granville St.	8/26-9/6	9/10	9/12	2,070	172

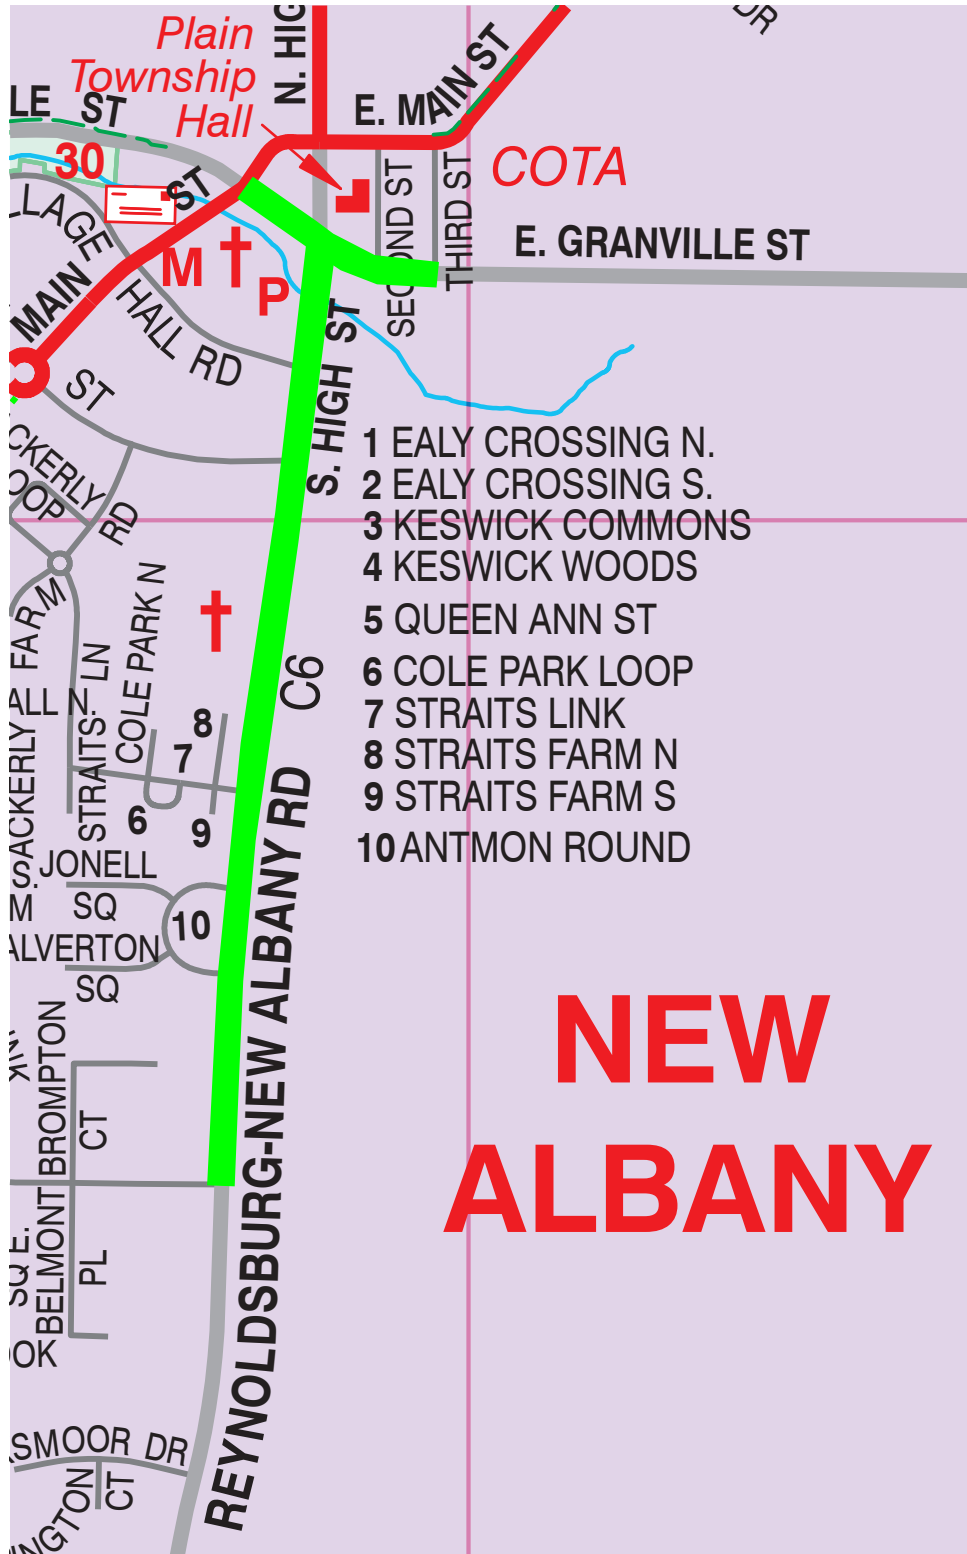


# Location 8 MOT Plan

Location 8						
Plan #	Street Name	Concrete Date	Milling Date	Paving Date	SY	Tons
9	Camile Rd.	9/9-9/13	9/18	9/23	860	72
12	Decker Dr.	9/9-9/13	9/18	9/23	2,276	190
25	Jersey Dr	9/9-9/13	9/18	9/23	2,444	204
52	Sugarwood Dr.	9/9-9/13	9/19	9/24	2,586	215
53	Triplet Sq.	9/9-9/13	9/19	9/24	3,724	310

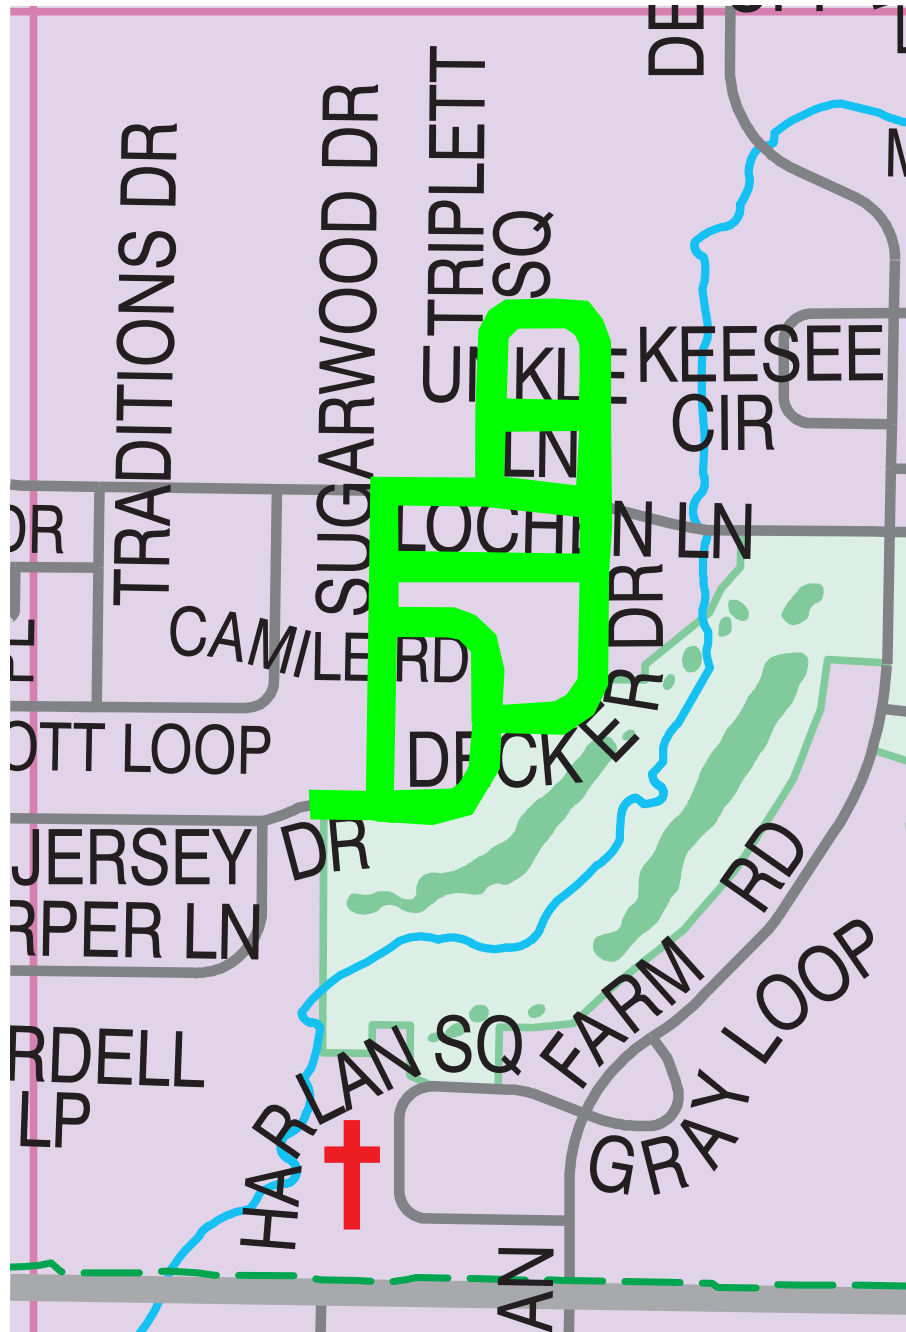



# Crack Sealing MOT Plan

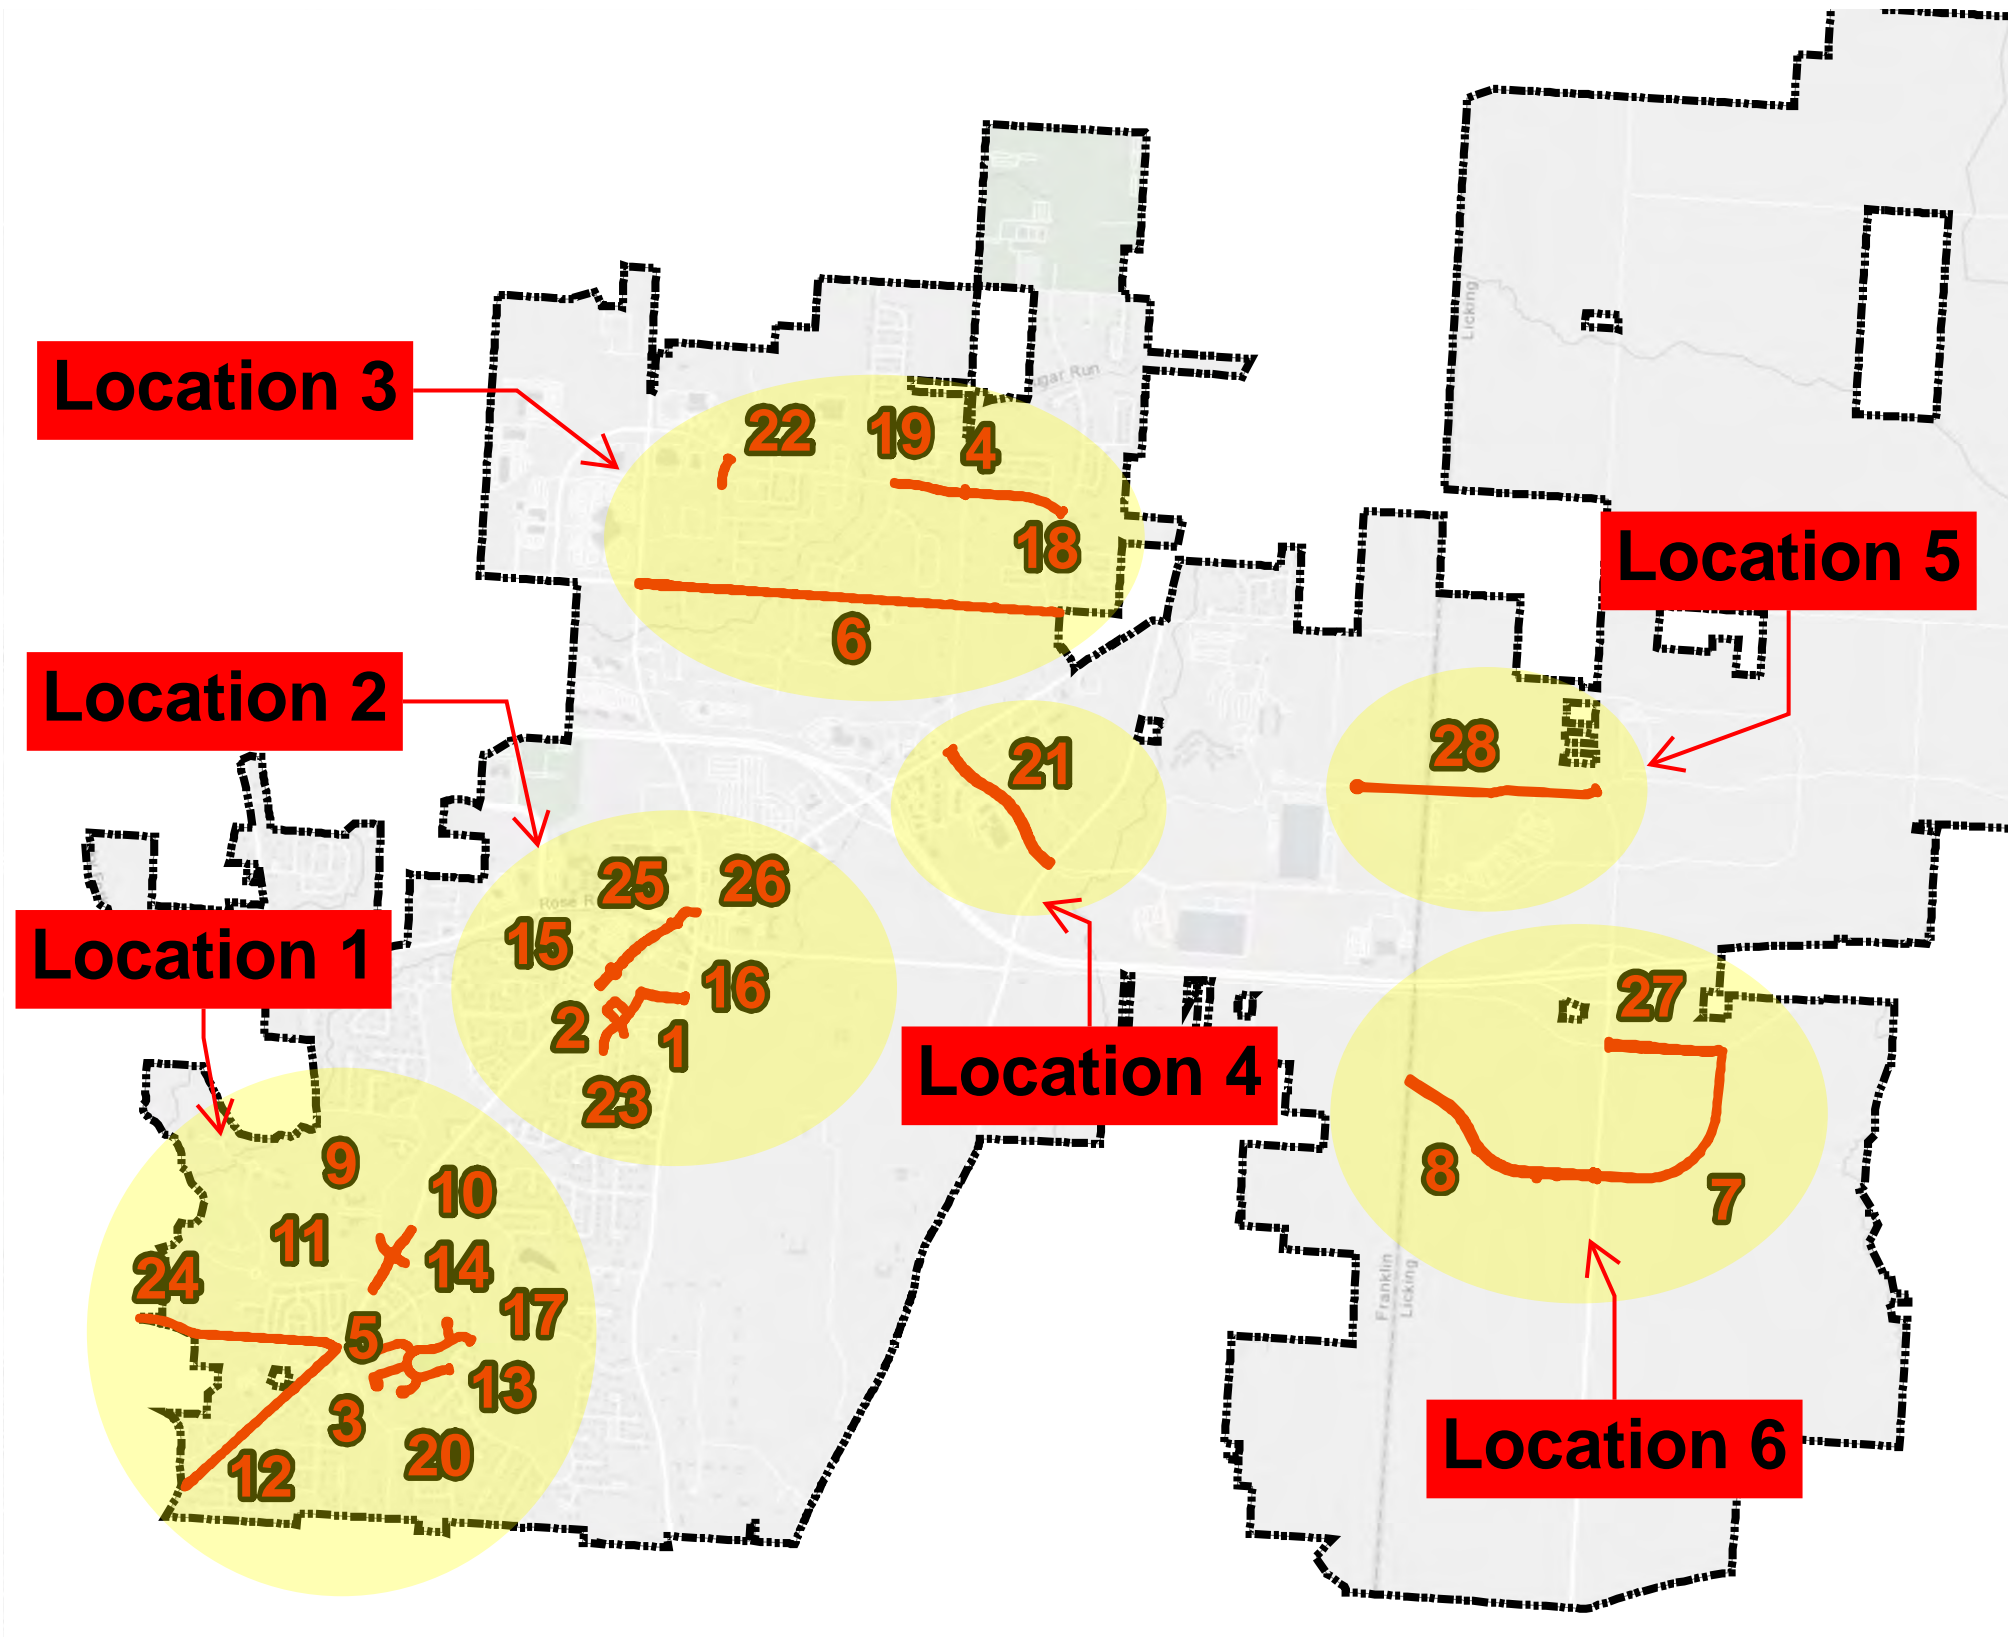


Plan #	Road Name	SY	Location
1	Ackerly Farm Rd	4,064	2
2	Ackerly Loop	1,891	2
3	Ashcombe	2,702	1
4	Bevelhymer Rd	406	3
5	Biddick	3,011	1
6	Central College Rd.	21,999	3
7	Ganton Parkway	13,651	6
8	Ganton Parkway W	26,452	6
9	Greensward Rd.	1,451	1
10	Johnstown Rd.	2,088	1
11	Johnstown Rd.	2,618	1
12	Johnstown Rd.	12,545	1
13	Lambton Green N	6,411	1
14	Lambton Park Rd.	843	1
15	Main/Market Roundabout	2,643	2
16	Market St.	4,693	2
17	Molland	1,290	1
18	New Albany Rd E	6,128	3
19	New Albany Rd E	4,355	3
20	Purdey Ct.	1,668	1
21	Smith's Mill Rd.	17,028	4
22	Souder Rd.	1,589	3
23	Straits Ln.	443	2
24	Thompson Rd.	10,102	1
25	W. Main St.	5,991	2
26	W. Main St.	1,833	2
27	Worthington Rd.	13,223	6
28	Innovation Campus Way West	15,716	5

Location	Working Dates
1	9/18-9/20
2	9/23-9/25
3	9/26-9/27
4	9/30-10/1
5	10/2-10/3
6	10/4-10/7



# Reclaimite MOT Plan

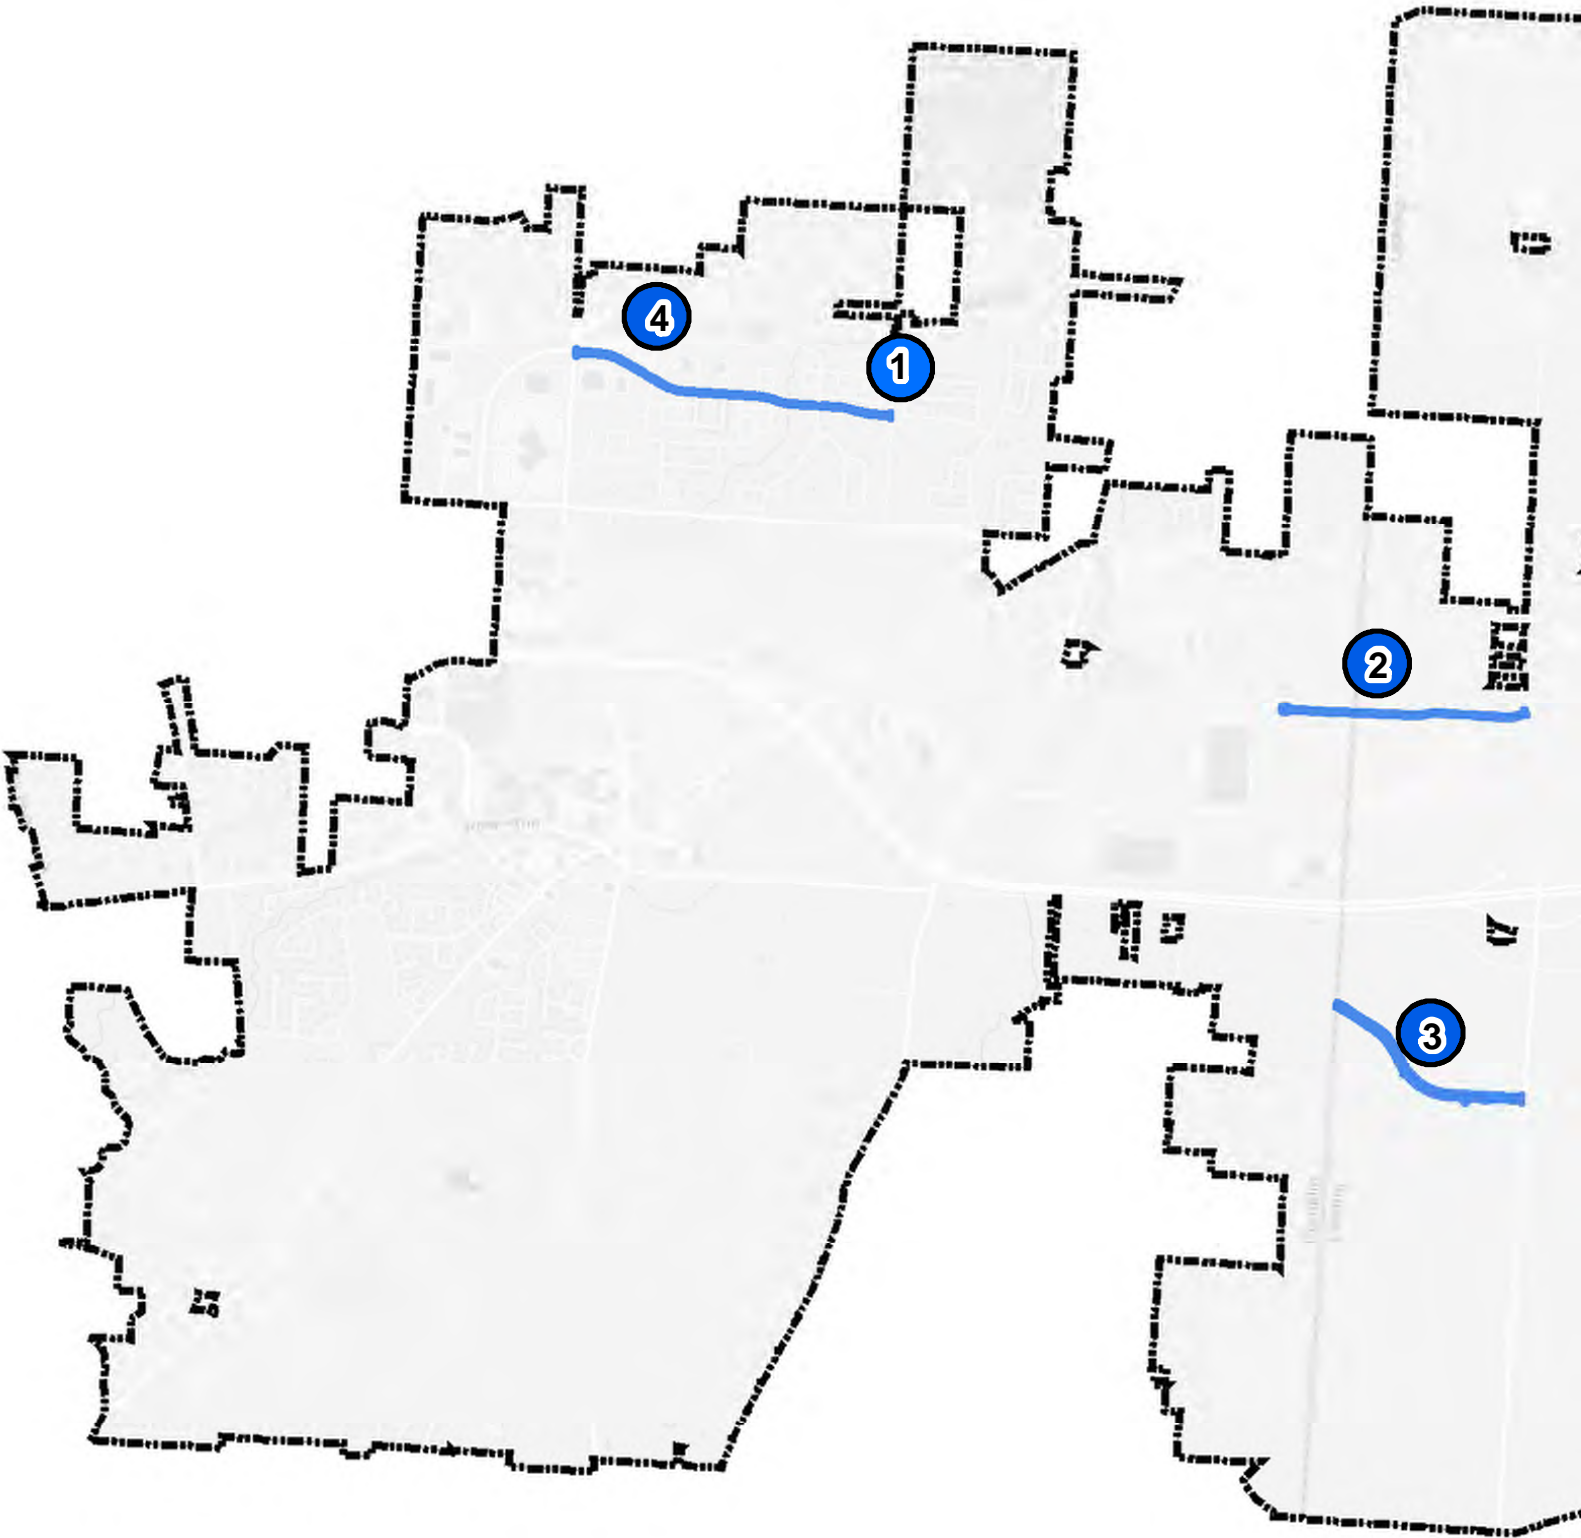

Plan #	Street Names	Working Dates
1	New Albany Rd E	10/1
2	Innovation Campus Way West	10/2
3	Ganton Parkway W	10/3
4	New Albany Rd E	10/1

# Striping MOT Plan

Location	Striping Date
1	10/14-10/16
2	10/17
3	10/24-10/25
4	10/21-10/23
5	10/18

